Stoughton Fire Headquarters & Public Health
30 Freeman Street
Stoughton, MA 02072

PAGE
BUILDING CONSTRUCTION CO.

ID	Task Name	Duration	Start	Finish	% Complete
1	**Milestones**	**253 days**	**Tue 11/26/24**	**Tue 12/2/25**	**0%**
10	**Permitting**	**33 days**	**Tue 11/26/24**	**Mon 1/13/25**	**100%**
15	**MassDEP**	**10 days**	**Mon 12/30/24**	**Mon 1/13/25**	**100%**
17	AQ-04 10-Day Notification	10 days	Mon 12/30/24	Mon 1/13/25	100%
19	AQ-06 10-Day Notification	10 days	Mon 12/30/24	Mon 1/13/25	100%
21	**Pre-Construction**	**92 days**	**Mon 12/2/24**	**Mon 4/14/25**	**27%**
248	**Construction**	**221 days**	**Fri 12/27/24**	**Fri 11/14/25**	**3%**
249	**Mobilization**	**14 days**	**Mon 12/30/24**	**Fri 1/17/25**	**67%**
250	Modify Existing Fences	2 days	Thu 1/16/25	Fri 1/17/25	0%
255	Erosion Controls	1 day	Thu 1/16/25	Thu 1/16/25	0%
258	**Interior Abatement and Demolition**	**35 days**	**Mon 1/6/25**	**Tue 2/25/25**	**14%**
259	**2nd Floor**	**25 days**	**Mon 1/6/25**	**Mon 2/10/25**	**40%**
261	Abatement	10 days	Mon 1/13/25	Mon 1/27/25	50%
262	Demolition	10 days	Tue 1/28/25	Mon 2/10/25	0%
263	**1st Floor**	**25.25 days**	**Tue 1/14/25**	**Thu 2/20/25**	**15%**
264	Select Demolition	5 days	Tue 1/14/25	Wed 1/22/25	75%
265	Abatement	10 days	Wed 1/22/25	Wed 2/5/25	0%
266	Demolition	10 days	Wed 2/5/25	Thu 2/20/25	0%
267	**Mezzanine**	**26.25 days**	**Mon 1/13/25**	**Thu 2/20/25**	**9%**
268	Select Demolition	2 days	Mon 1/13/25	Tue 1/14/25	100%
269	Abatement	10 days	Wed 1/22/25	Wed 2/5/25	0%
270	Demolition	10 days	Wed 2/5/25	Thu 2/20/25	0%
271	**Basement**	**25 days**	**Tue 1/21/25**	**Tue 2/25/25**	**0%**
272	Select Demolition	5 days	Tue 1/21/25	Mon 1/27/25	0%
273	Abatement	10 days	Tue 1/28/25	Mon 2/10/25	0%
275	**Addition**	**28 days**	**Wed 1/15/25**	**Tue 2/25/25**	**5%**
276	Select Demolition (N/A)	1 day	Wed 1/15/25	Wed 1/15/25	100%
277	Abatement	10 days	Tue 1/28/25	Mon 2/10/25	0%
280	**Exterior Abatement and Demolition**	**51 days**	**Tue 1/21/25**	**Wed 4/2/25**	**0%**
281	**North Elevation**	**16 days**	**Tue 1/21/25**	**Tue 2/11/25**	**0%**
282	Select Demolition	5 days	Tue 1/21/25	Mon 1/27/25	0%
283	Abatement - Demo Windows / Exterior Openings (11)	10 days	Tue 1/28/25	Mon 2/10/25	0%
284	Temp Protection	10 days	Wed 1/29/25	Tue 2/11/25	0%
285	**East Elevation**	**16 days**	**Tue 1/28/25**	**Wed 2/19/25**	**0%**
286	Select Demolition	5 days	Tue 1/28/25	Mon 2/3/25	0%
287	Abatement - Demo Windows / Exterior Openings (8)	10 days	Tue 2/4/25	Tue 2/18/25	0%
288	Temp Protection	10 days	Wed 2/5/25	Wed 2/19/25	0%
301	**Site Demolition**	**45 days**	**Fri 1/3/25**	**Mon 3/10/25**	**39%**
303	Remove Shed / Demo Foundation	2 days	Tue 1/28/25	Thu 1/30/25	0%
313	**Utilities**	**94 days**	**Fri 12/27/24**	**Tue 5/13/25**	**5%**
314	**Electric Service**	**94 days**	**Fri 12/27/24**	**Tue 5/13/25**	**10%**
316	Scheduling / Design	30 days	Wed 1/8/25	Fri 2/21/25	25%
351	**Water Service**	**45.5 days**	**Tue 2/4/25**	**Wed 4/9/25**	**0%**
352	Service Request	0 days	Tue 2/4/25	Tue 2/4/25	0%
353	Scheduling	30 days	Tue 2/4/25	Wed 3/19/25	0%

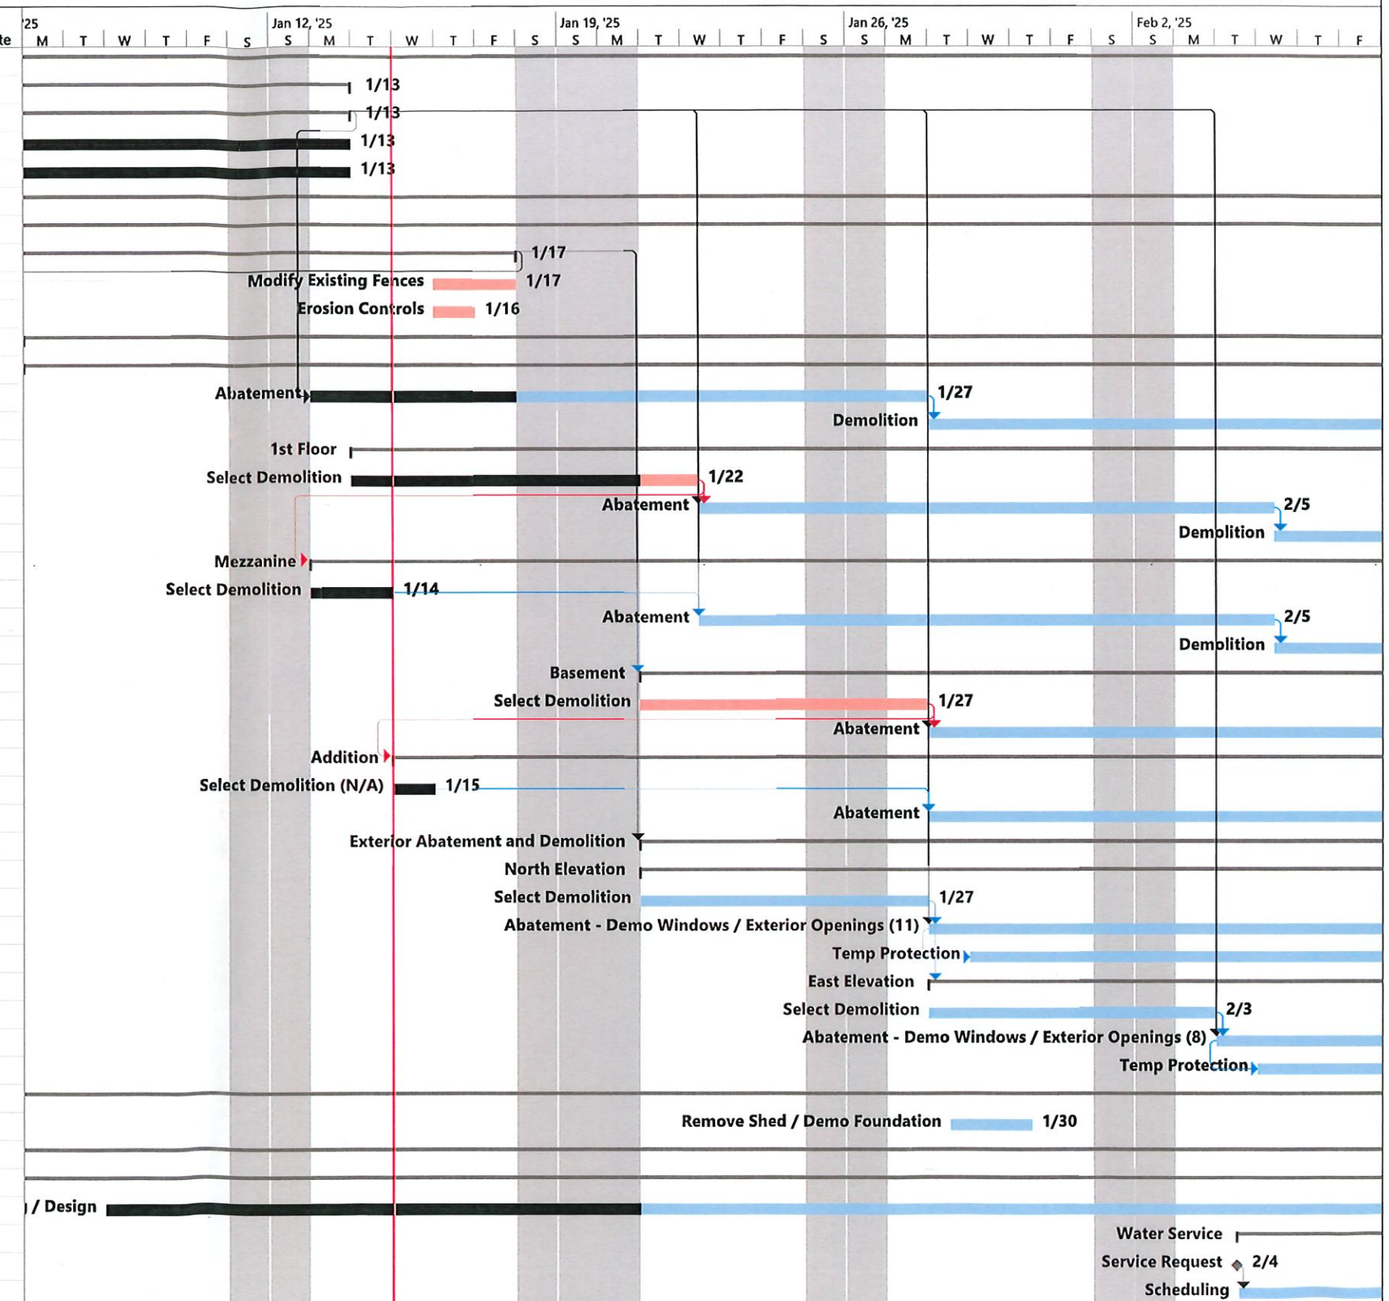

Wed 1/15/25
